10-12 CAMBRIA ROAD



Final Project Report to


Newton Community Preservation Committee

12 October 2017

Citizens for Affordable Housing in Newton Development Organization, Inc

Project narrative & financial summary are included at the end of this presentation,


Neighborhood Map

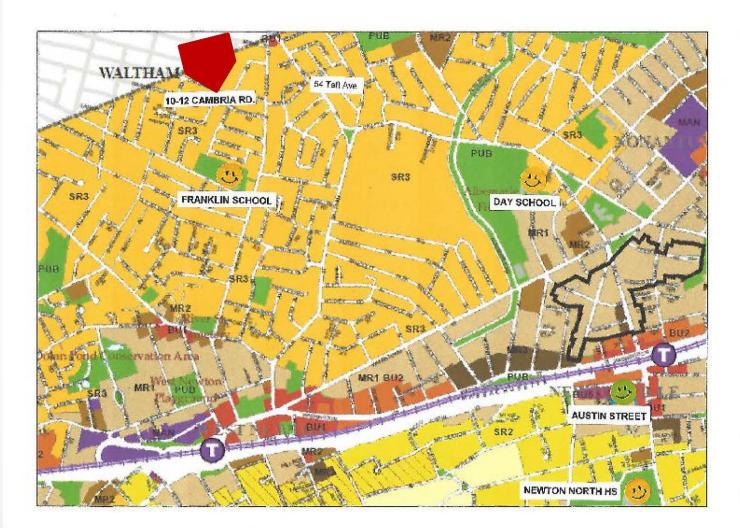

Renovations to existing two-family home:

- Remove/remediate: lead paint, asbestos, mold
- New roof and heating system
- Repair/seal: chimney, siding, trim, gutters, downspouts, decking & structural supports, plumbing lines and valves and electrical connections
- Second-floor kitchen: repartition, new cabinets and appliances
- Basement: remove ceilings, wall finishes, and asbestos floor tile; repair partitions; replace rotted sills and stairs; provide proper access to electrical panes
- Construction began December 2016
- Construction completed June 2017

Only significant change: redesigned second-floor kitchen

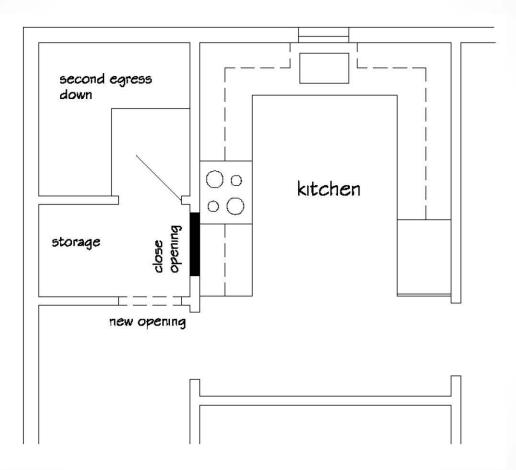

Budgeted vs. Actual Costs

USES	BUDGET	ACTUAL			
Acquisition	\$610,000	\$610,000			
Construction (incl. Environmental Remediation)	\$148,528	\$164,786			
Soft Costs					
Architect/Engineer, Survey, Environmental	\$22,000	\$10,554			
Building Permits	\$2,430	\$0			
Legal, Title & Recording, Appraisal	\$6,600	\$0			
Real Estate Taxes	\$5,500	\$10,701			
Insurance (Liability, Builder's Risk)	\$7,500	\$6,827			
Loan Interest	\$20,112	\$16,763			
Marketing and Lease-up	\$0	\$2,280			
Utilities	\$0	\$3,477			
Soft Cost Contingency	\$6,414				
Soft Costs Subtotal	\$70,556	\$50,601			
Developer Overhead/Fee	\$66,327	\$66,327			
Replacement Reserve	\$10,000	\$10,000			
TOTAL PROJECT COSTS	\$905,410	\$901,714			

Funding Sources

SOURCES	BUDGET	ACTUAL
City of Newton - CDBG	\$ 189,293.00	\$ 189,293.00
City of Newton - HOME	\$ 195,000.00	\$ 195,000.00
Newton CPA Program	\$ 471,117.00	\$ 471,117.00
Charlesbank Homes (Foundation Grant) -	\$ 50,000.00	\$ 50,000.00
** funds not used for project direct costs were		
added to replacement reserve		
TOTAL SOURCES	\$ 905,410.00	\$ 905,410.00





1st floor







before



after





after







79-B Chapel Street Newton, MA 02458 Phone: 617-923-3505 Fax: 617-923-8241

To: Elizabeth Valenta and Alice Ingerson From: Jennifer Van Campen Date: September 14, 2017 Re: 10-12 Cambria Rd.

The Cambria Road project entailed the acquisition and renovation of an existing two-family home. It received a commitment of \$384,293 in HOME and CDBG funds as well as \$471,117 in CPA funds. A private foundation also provided a \$50,000 grant. The General Contractor was selected through the City of Newton procurement process and construction began in Fall 2016.

The project was substantially completed in late Spring 2017. Tenants were selected through an affirmatively marketed lottery process. There was a preference for homeless families. Approximately 290 applications were received. 88 had homeless preference. Final tenants selected include:

a) Two bedroom (50% AMI unit) – Homeless preference family of 2, race not reported b) Two bedroom (80% AMI unit) – Family of 3, race Black

Both households are mobile voucher holders. The first tenant moved in August 1st and the second will move in October 1st. The tenant selection process was slow due to the requirement that potential tenants be interviewed for appropriateness for CAN-DO's supportive services. Additionally, more than half of the applicants were screened out due to insufficient income to pay the rent. In order to effectively serve homeless households CAN-DO projects in the future will need to identify some kind of rental subsidy.

The final total development cost was \$901,713.46, slightly under the original budget. We would like to request that CAN-DO be allowed to retain the balance (coming from the Charlesbank Home Foundation grant) to add a small extra cushion to our Reserves for the project.

10-12 CAMBRIA	9/12/2017			-	Total Req.		
			ORIGINAL		FINAL	_	
DEVELOPMENT BUDGET			BUDGET	FYC	PENDITURES		riance over der) budget
		<u> </u>				(un	uer) buuget
SUBTOTAL - ACQUISITION COST		\$	610,000.00		610,000.00		-
CONSTRUCTION COSTS:				_			
Direct Construction Costs		\$	135,025.00		154,025.67	1	19,000.67
Environmental Remediation		\$	135,025.00		10,760.00		19,000.07
Construction Contingency	10%	-	13,502.50		-		(13,502.50)
Total Construction	10/0	\$	-	\$	164,786	\$	16,258
		Ş	140,527.50	Ş	104,780	Ş	10,230
TOTAL ACQUISITION AND CONSTR		ć	758,527.50	\$	774,786	\$	16,258
TOTAL ACQUISITION AND CONSTR		Ş	758,527.50	Ş	//4,/80	Ş	10,250
SOFT COSTS							
Architect/Engineer		\$	20,000.00		9,311.86	1	(10,688.14)
Survey		\$	2,000.00		700.00		(1,300.00)
Building Permits		\$	2,430.00		-		(2,430.00)
Legal		\$	3,500.00				(3,500.00)
Title and Recording		\$	2,500.00		_		(2,500.00)
Real Estate Taxes		\$	5,500.00		10,700.98		5,200.98
Liabilty Insurance		\$	4,000.00		5,272.89		1,272.89
Builder's Risk insurance		\$	3,500.00		1,554.00		(1,946.00)
Appraisal		\$	600.00		-		(600.00)
Loan Interest	8 months	\$	20,112.00		16,762.84		(3,349.16)
Pre-development							
Relocation							
Marketing and Lease-up		\$	-		2,280.00		2,280.00
Utilities		\$	-		3,476.92		3,476.92
Total		\$	64,142.00		50,059.49		(14,082.51)
Soft Cost Contingency	10%	\$	6,414.20		541.60		(5,872.60)
Subtotal: SOFT COSTS		\$	70,556.20	\$	50,601.09		(19,955.11)
Subtotal: Acquis., Const.,							
and Gen. Development		\$	829,083.70	\$	825,386.76		(3,696.94)
>Developer Overhead/Fee	8%	\$	66,326.70		66,326.70		-
Fund Replacement Reserve		\$	10,000.00		10,000.00		-
TOTAL DEVELOPMENT COSTS		\$	905,410.40		901,713.46		(3 <i>,</i> 696.94)

10-12 CAMBRIA	9/12/2017					
	Original				F	Remaining
FUNDING SOURCES:	Budget	Re	eq'd To date	Final Req. F		Funds
City of Newton - CDBG	\$ 189,293.00	\$	187,400.07	\$ 1,892.93	\$	-
City of Newton - HOME	\$ 195,000.00	\$	193,050.00	\$ 1,950.00	\$	-
CPA GRANT	\$ 471,117	\$	424,066.10	\$ 47,050.90	\$	-
Charlesbank Homes	\$ 50,000	\$	-	\$ 46,303.46	\$	3,696.54
	\$ 905,410.00	\$	804,516.17	\$ 97,197.29	\$	3,696.54
TOTAL SOURCES		\$	905,410.00			
