


LOUISE LEVINGSTON COVE IMPROVEMENTS PROJECT @ CRYSTAL LAKE

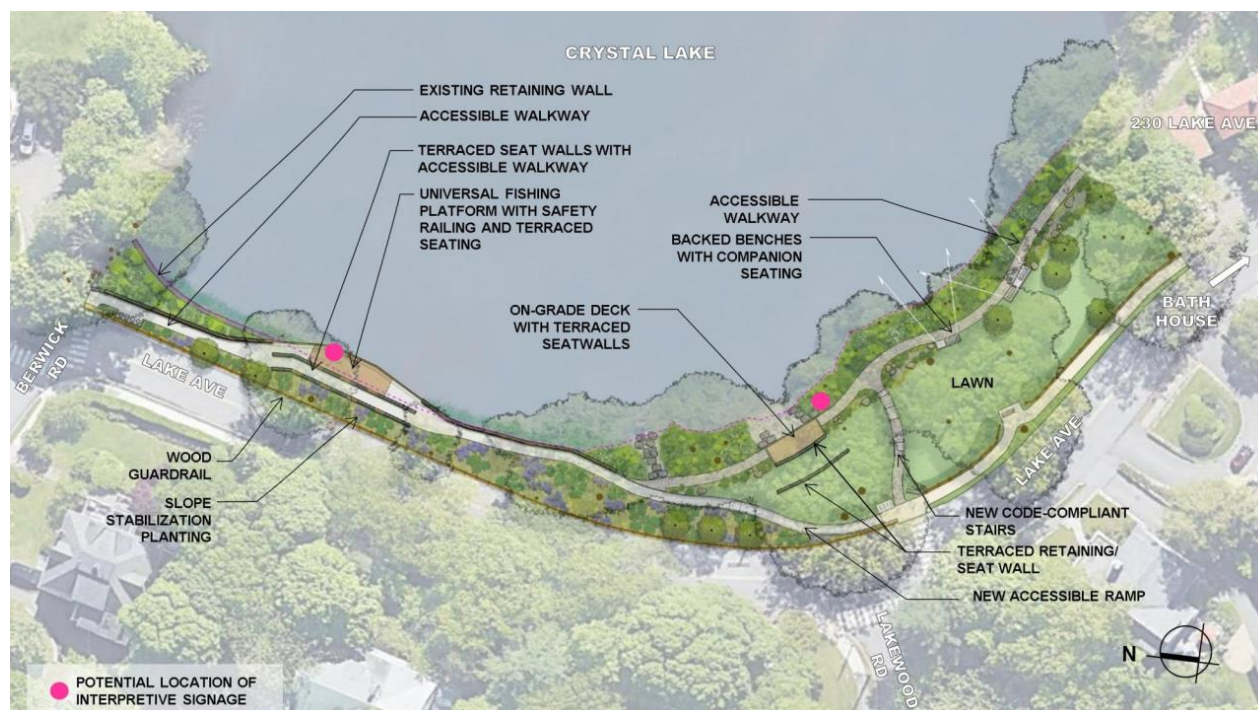

Project Update:

- Park closed as of November 28th
- Construction work began the week of December 5th
- **Construction contractor:** [SUMCO ECO-CONTRACTING](#)
- **Public construction bid:** [BID 23-25](#)
- **Expected completion date:** June 2023
- **Project funding source:** Newton Community Preservation Act (CPA) Funds
- **Project Narrative and other Information:** [Newton Conservators Newsletter Project Write-up](#)

Weeks of January 30th, 2023 through February 10th, 2023: Continued site preparation; Park boulder inventory; retaining wall subsurface preparation; rain garden outfall construction





Weeks of January 9th, 2023 through January 23rd, 2023: Continued site preparation; Park boulder inventory; cantilever deck base preparation, rain garden subgrade preparation; rain garden overflow structure preparation









Weeks of January 9th, 2022 through January 16th, 2023: Continued site preparation; Tree pruning; Park boulder inventory



Weeks of December 26th, 2022 through January 5th, 2023: Continued removal of concrete walkway; Removal of existing stonedust path; subgrade excavation for rain gardens and new pathways; Continued micropile drilling and grouting; Additional micropile load tests.





Week of December 12th, 2022: Continued removal of concrete walkway; micropile casings and equipment arrival; Load test micropile drilled; Load test prepared; micropile drilling begins.












Week of December 5th, 2022: Erosion controls and tree protection installed; handrails removed; existing low retaining wall removed; partial removal of concrete walkway; Staging area at Crystal Lake Park prepared.





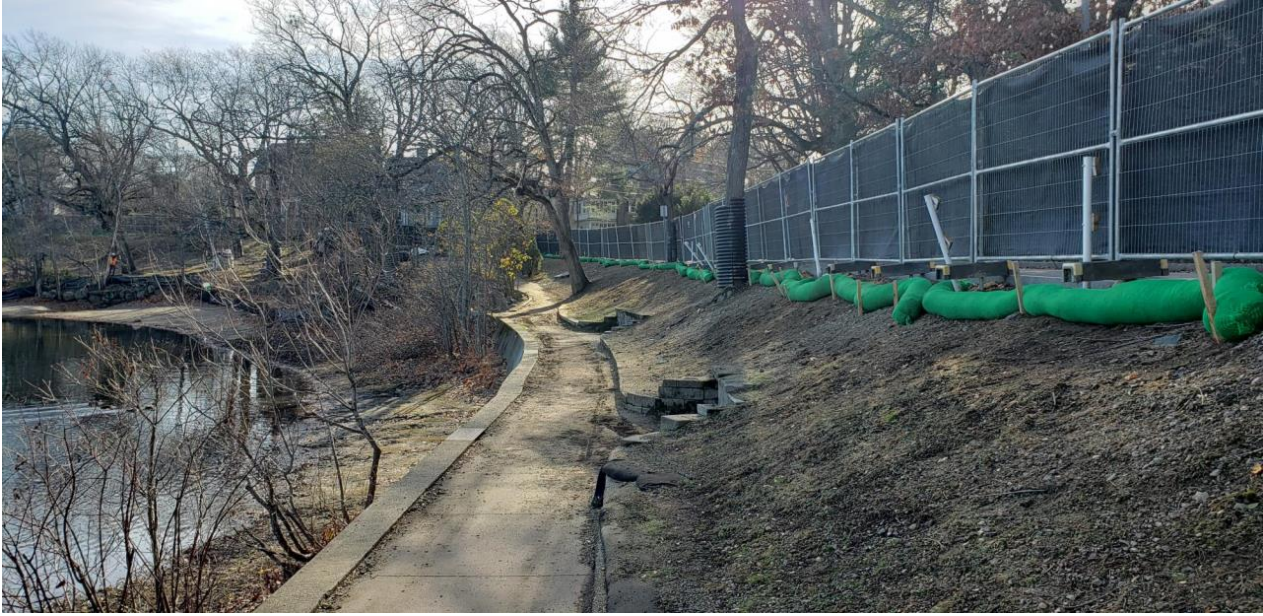



Week of November 28th, 2022: Construction fence and windscreen installed



Project Documents:

[2021 09 22 Levingston Cove Permitting Set](#)

[Levingston Cove Conservation Commission Order Of Conditions - Special Conditions](#)

[Massachusetts Historic Commission Permit Application- Levingston Cove](#)

[Levingston Cove CH 91](#)

[Levingston Cove CPC Construction Funding Meeting Presentation](#)

[Levingston Cove Parks Commission 5-20-19](#)

[Levingston Cove Mtg 04-22-2019](#)

[Levingston Cove- Parks Commission 4-23-18](#)
